


ID	Task Name	Duration	Start	Finish	Predecessors
1	Graton CSD - Sewer R&R - Phase 1	111 days	Thu 8/10/23	Fri 1/19/24	
2	Kickoff Meeting	0 days	Thu 8/10/23	Thu 8/10/23	
3	Condition Assessment	110 days	Fri 8/11/23	Fri 1/19/24	
4	Digitize 1976 Asbuilts and Setup FieldMaps	9 days	Fri 8/11/23	Wed 8/23/23	
5	MH Field Locating and Inspection	5 days	Thu 8/24/23	Wed 8/30/23	4
6	Perform Pump Station Inspections	0 days	Mon 8/21/23	Mon 8/21/23	
7	Develop CCTV Plan	10 days	Thu 8/31/23	Thu 9/14/23	5
8	Perform cleaning and CCTV	15 days	Mon 9/18/23	Fri 10/6/23	7
9	Prepare Draft Condition Assessment TM	4 wks	Mon 10/9/23	Fri 11/3/23	8
10	District Review Period	2 wks	Mon 11/6/23	Fri 11/17/23	9
11	Prepare Final Condition Assessment TM	2 wks	Mon 11/20/23	Tue 12/5/23	10
12					
13	Coordination with Water Board	100 days	Fri 8/25/23	Fri 1/19/24	
14	Meeting with Water Board to discuss scope, fee, sche	0 days	Fri 8/25/23	Fri 8/25/23	
15	Submittal of Q1/Q2 Report	0 days	Thu 8/31/23	Thu 8/31/23	
16	Submittal of Q3 Report and Disbursement Request	0 days	Wed 10/18/23	Wed 10/18/23	
17	Submittal of Q4 Report and Disbursement Request	0 days	Fri 1/19/24	Fri 1/19/24	

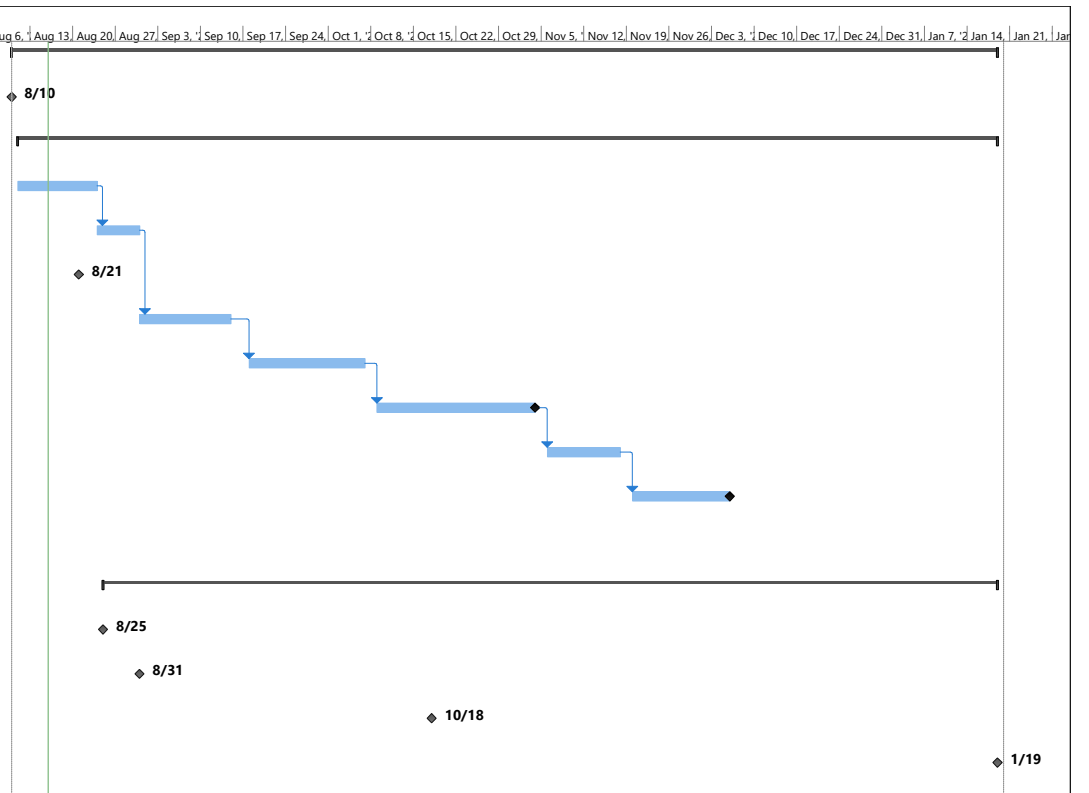

Project: Graton CSD RR Schedu Date: Wed 8/16/23	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
